


Oxford Biochemistry Phase 2 BUILD SEQUENCE LOOK AHEAD


NOVEMBER 2018

Guide wall commences

Piling mat commences

WC 12 November 18

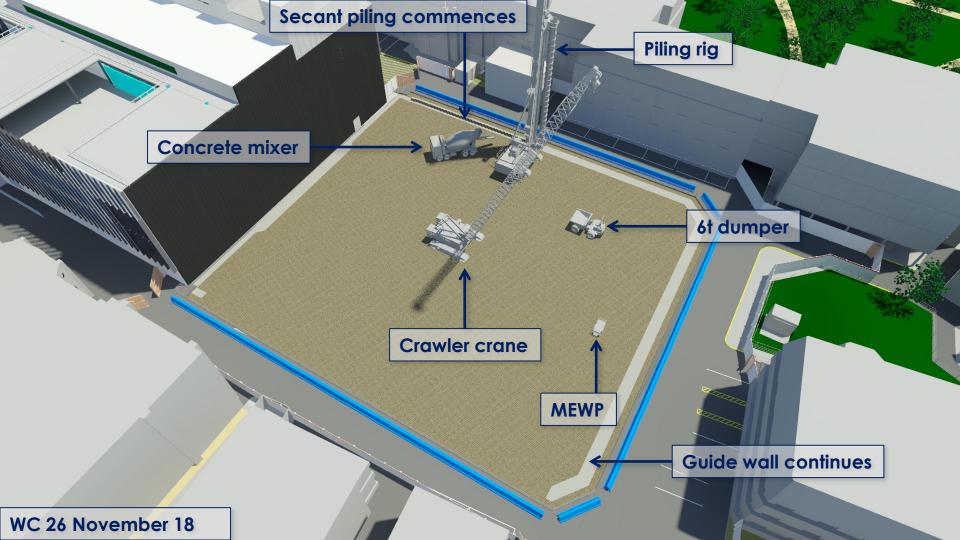

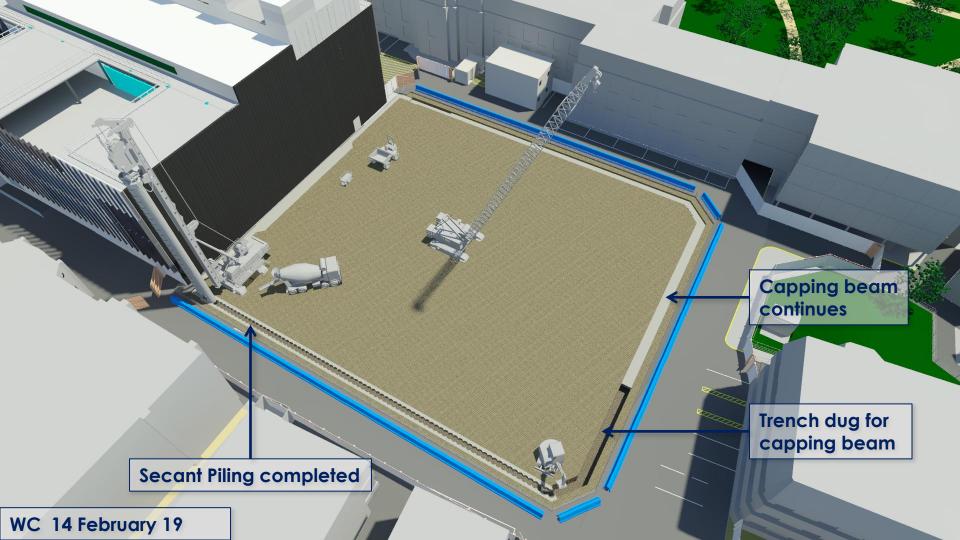

Excavation to underside of capping beam – approx 1.5m depth (+61.05m)

WC 25 February 19

Props installed at capping beam level

WC 25 February 19

Existing sheet piles to be removed locally to enable installation of props Excavation continues to approx 5.5m depth (+56.95m)

Cut sheet piles locally to gain access, install raking props

WC 4 March 19
