



OXFORD BIOCHEMISTRY COMPLETION

Registered Office: Bridge Place, Anchor Boulevard, Admirals Park, Crossways, Dartford, Kent DA2 6SN. Registration Number: 4309402



Update: ISSUE 7

January 2020

Progress Update/Key Milestones



Introduction

Welcome to the construction newsletter for Biochemistry Completion from the main contractor Laing O'Rourke (LOR).

The site is registered with the Considerate Constructor Scheme, a voluntary scheme set up to improve the image of the UK's construction industry. LOR will be audited throughout the construction phase of the project on a number of topics including the environment, safety, respect in the community, communication and accountability.

Main roof works progressing well.

Fit out works are continuing with more trades coming to site doing various works.


Basement and Lower ground fit out is now in progress with screeding taking place within the lower floors.

The glass installation of the North façade is making good progress with planned completion being Friday 24th Jan.


The flow of deliveries will continue as works progress. The Logistic team will manage and coordinate these deliveries .

Project Overviews

Biochemistry Phase 2 construction - looking north-west 2019-12-10 16:04:42

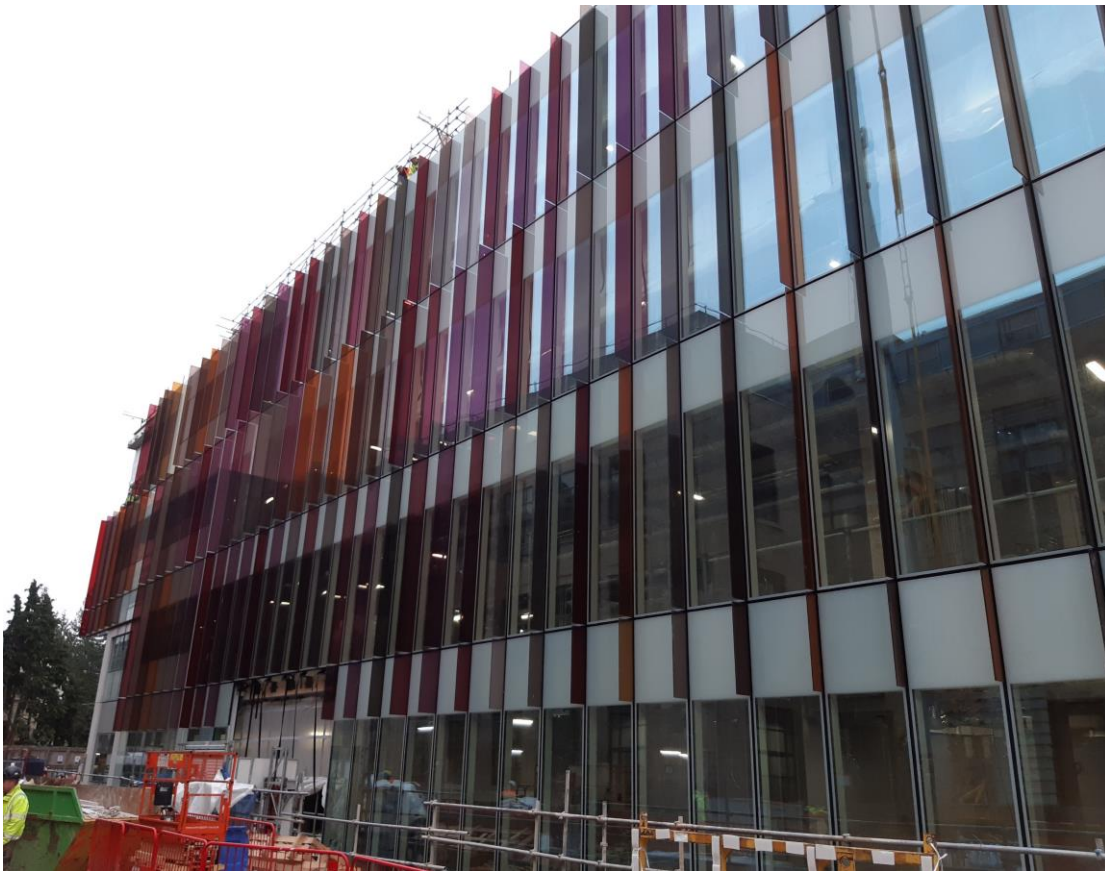

Project Overviews

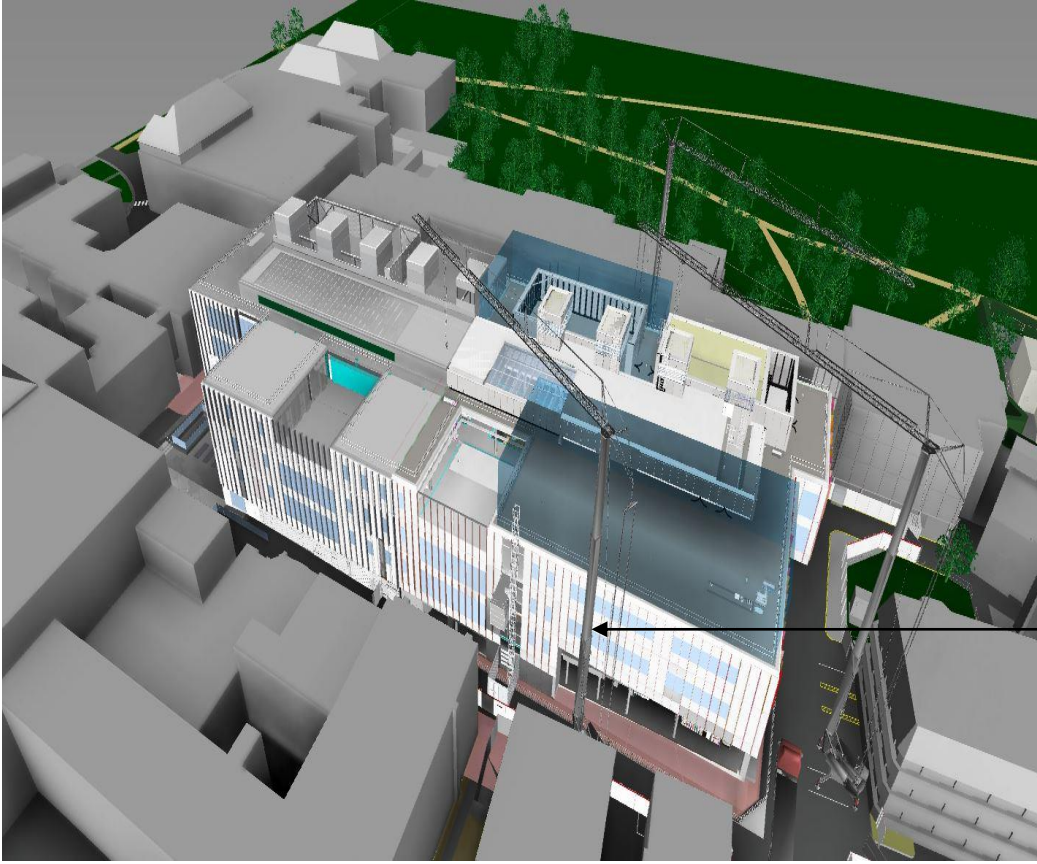

New Crane location
from Tues Jan 28th.



Project Overviews



Enabling construction works
commenced Main construction works
commenced Construction concludes

October 2018
November 2018
Christmas 2020

Programme of Works

The Biochemistry Completion works are planned to last 109 weeks, from 12th November 2018.

We are now in week 63 of the planned programme with works progressing well and being 3 weeks ahead of this programme

Weekend working is anticipated.

Forthcoming Events

The installation of MEP modules will continue and the fitting out of floors.


The self-erecting crane is being re-located from the North elevation to the 2nd of it's 3 planned locations, this being at the South elevation of the building. This move is planned for Tuesday 28th January.

www.medsci.ox.ac.uk/biochemistry-2-updates


Contact Us

If you have any questions regarding the above or the Biochemistry project please do not hesitate to contact the following:-

ROB COOPER
Project Leader Laing
O'Rourke

 Tel: 07765612916

Lee Hooper
Logistics manager
Laing O'Rourke

 Tel: 07385038421
