



# OXFORD BIOCHEMISTRY COMPLETION

Registered Office: Bridge Place, Anchor Boulevard, Admirals Park, Crossways, Dartford, Kent DA2 6SN. Registration Number: 4309402



Update: ISSUE 9

July 2020

## Progress Update/Key Milestones



### Introduction

Welcome to the construction newsletter for Biochemistry Completion from the main contractor Laing O'Rourke (LOR).

The site is registered with the Considerate Constructor Scheme, a voluntary scheme set up to improve the image of the UK's construction industry. LOR will be audited throughout the construction phase of the project on a number of topics including the environment, safety, respect in the community, communication and accountability.

WE have carried out a COVID-19 Risk Assessment, and works continue on site, in line with the latest guidelines.

Fit out works are progressing well on all floors.

The façade is nearing completion. We have started 2 key trades recently, Resin flooring and Laboratory furniture.


We have Power on in the building.

The flow of deliveries will continue as works progress. The Logistic team will manage and coordinate these deliveries .

# Project Overviews



East soffit install complete

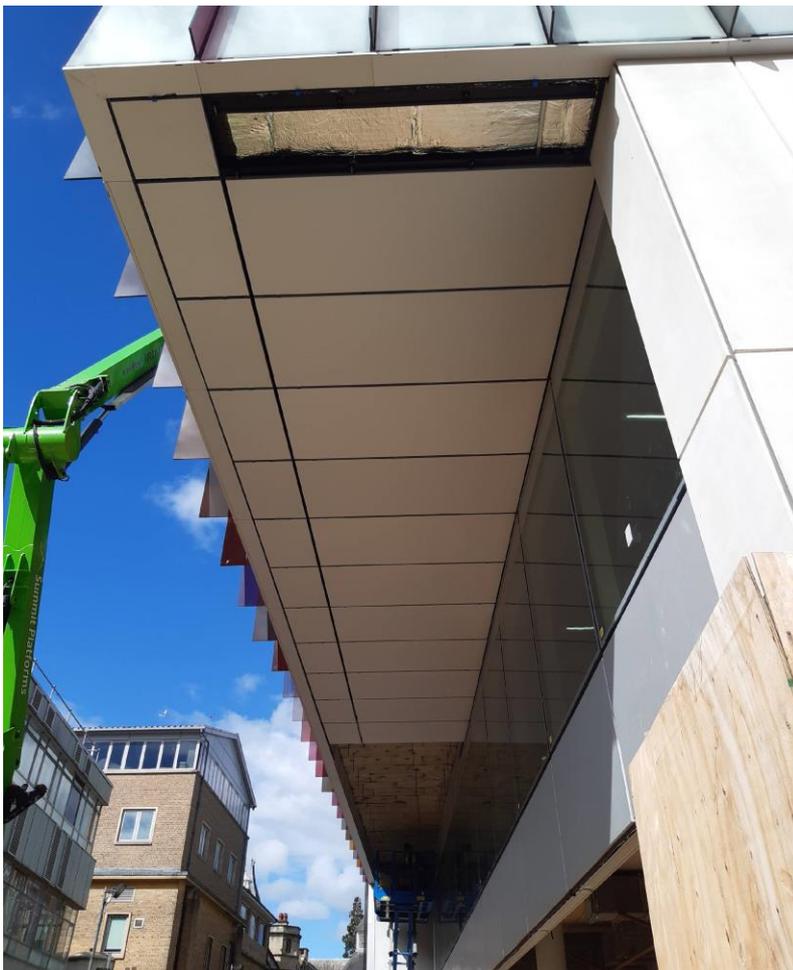

South soffit works on-going but nearing completion.

# Project Overviews



Resin being put down on lower floors with Ground level being laid w/c 6<sup>th</sup> July 2020



Floor protection being installed after resin has been laid.

# Project Overviews



LabFlex furniture  
being installed on  
ground level.



Enabling construction works	October 2018
commenced Main construction works	November 2018
commenced Construction concludes	Christmas 2020

## Programme of Works

The Biochemistry Completion works are planned to last 116 weeks, from 12<sup>th</sup> November 2018.

We are due to complete 1<sup>st</sup> Feb 2021.

Site has remained fully open during the Covid-19 pandemic with numerous safety precautions implemented by the LOR team in line with Government advice. These precautions are still in place including the 2m social distancing where possible.

## Forthcoming Events

[www.medsci.ox.ac.uk/biochemistry-2-updates](http://www.medsci.ox.ac.uk/biochemistry-2-updates)

## Contact Us

If you have any questions regarding the above or the Biochemistry project please do not hesitate to contact the following:-

ROB COOPER  
Project Leader Laing  
O'Rourke

 Tel: 07765612916

Lee Hooper  
Logistics manager  
Laing O'Rourke

 Tel: 07385038421
